

KANE

Weekly Update

DATE: 7th of June 2024

MostynCopper



Waypoint 

WORKS COMPLETED THIS WEEK

Building A

- Backfilling, drainage material and drainage cell to precast retaining walls
- Waterproof membrane to precast retaining walls
- Installation of Services to Upper Floor
- Detailed Excavation to the West of Building A Grandstand for Slats and Precast Panels
- Upper Floor Setout Works
- Screw Piling Installation to Ground Floor South SOG Pour 1
- Commence of Hydraulic inground services installation to (Ground Floor South SOG Pour)
- Relocation of Temporary Fencing Western Boundary
- Stormwater works and Detailed Excavation to West External works

Building B

- Pour Footings & Beams for SOG Pour 4
- FRP Pour 4
- All service trades to complete service works on SOG Pour 4
- Completion of Set-down bolts and Hold bolts to SOG Pour 4
- Grouting, Pan filling, Installation of PT ducts and Grout hoses to TMJ reinforcement – Upper Pour 1
- Formwork to suspended deck (Upper Floor Pour 2)
- Formwork Stripping to Upper Suspended Deck Pour 1
- Precast Setout for next Precast Install (LGF South)
- Waterproof membrane to precast retaining walls

WORKS PLANNED NEXT WEEK

Building A

- Formwork Stripping works Upper Floor (Suspended Deck) Pour 1- South
- Form deck & Edge boards (Coaches Box)
- Bottom & Top Steel (Coaches Box)
- All service trades to complete service works for (Coaches Box)
- Continue Installation of Stormwater Works (West)
- Raking Slab Precast Slat Setout works
- Detailed Excavation to Grandstand Plat Raking Beams
- Continue Hydraulic inground services installation to (Ground Floor South SOG Pour)

Building B

- Installation of South Panels and Internal Precast Plats
- Steel fixing to Bottom and Top steel (Upper Floor Pour 2)
- Complete edge boards to (Upper Floor Pour 2)
- Post Tensioning to Beams (Upper Floor Pour 2)
- All service trades to complete service works and Penetrations (Upper Floor Pour 2)
- Formworker to close Columns and Pour Verticals (Upper Floor Pour 2)
- Detailed Excavation for (SOG Pour 5)
- Structural Steel Set outworks

KANE

PROGRESS PHOTOS

05/06/2024 12:50:00



Building A

PROGRESS PHOTOS

05/06/2024 11:20:00



Building B

PROGRESS PHOTOS

4 Jun 2024 at 10:57:57 AM
311 Stone Mason Dr
Kellyville NSW 2155
Australia
Kellyville Memorial Park



Building A – Screw Piling Installation

PROGRESS PHOTOS

4 Jun 2024 at 12:56:44 PM
311 Stone Mason Dr
Kellyville NSW 2155
Australia
Kellyville Memorial Park



Building A – Screw Piling

PROGRESS PHOTOS

3 Jun 2024 at 3:47:00 PM
311 Stone Mason Dr
Kellyville NSW 2155
Australia
Kellyville Memorial Park



Building B – Columns and Beams Pour 4

KANE

PROGRESS PHOTOS



Building B – SOG Pour 4



KANE

PROGRESS PHOTOS



Building B – SOG Pour 4

PROGRESS PHOTOS

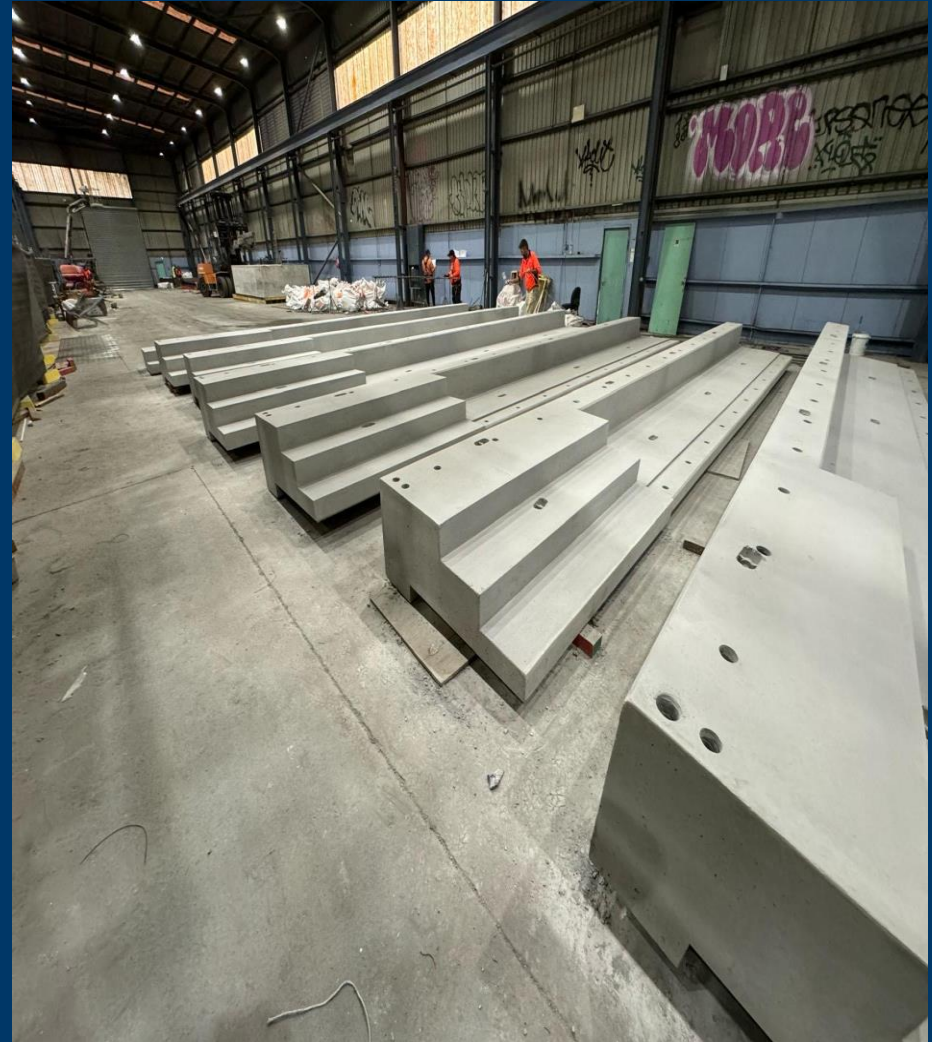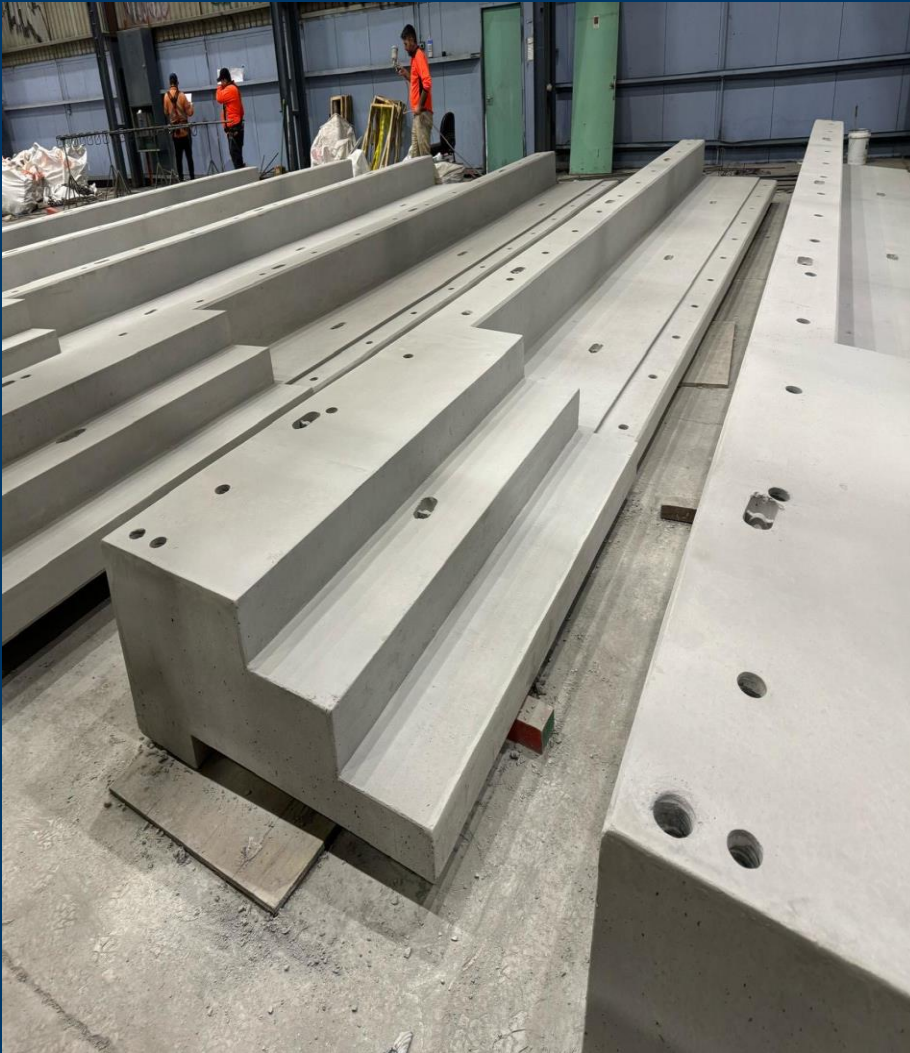

Building B - Precast Plats

PROGRESS PHOTOS

7 Jun 2024 at 9:36:34 AM
Kellyville NSW 2155
Australia
Kellyville Memorial Park

**Building B – Formwork Stripping Suspended
Deck Pour 1**



PROGRESS PHOTOS

7 Jun 2024 at 9:32:42 AM
Kellyville NSW 2155
Australia
Kellyville Memorial Park



Building B – Bondeck to Suspended deck
Pour 2
